

Hall C work from February 4th to April 1st 2008

Rev. 5

ID	Task Name	Status
1	<u>Hall C work for February and March 2008</u>	
2		
3	Disconnect and move BIG BITE magnet to Hall A.	Complete
4	RADCON support required	Complete
5	Move BIG BITE stand and base plate to bone yard.	Complete
6	RADCON support required	Complete
7	Move HES magnet boxes from the Test Lab to Hall C and unpack.	Complete
8	Move all HES boxes from the storage building to Hall C and unpack	Complete
9	Preassemble magnets, label parts and store.	Delayed
10	Strip G-0 FW and disassemble 10 detectors.	Active
11	Pack and remove all parts from Hall C	Active
12	Remove blue SOS magnet from pivot and move to the physics storage Bld.	Complete
13	RADCON support required	Complete
14	Fabricate and weld covers onto rails in prep. for concrete pad extension.	Delayed
15	RADCON support required	Delayed
16	Remove 24" gate valve on the downstream side	Active
17	RADCON support required	Active
18	Rmove absorber plates from BIG CAL	Complete

Project: 2008 Feb and March Hall C w Date: Tue 3/18/08 Rev. 5	Task		Project Summary	
	Split		External Tasks	
	Progress		External MileTask	
	Milestone		Split	
	Summary			

For information and changes contact the the Hall-C coordinator: Walter Kellner, ext. 5512, pager584-5512 , cell 592-1527

Hall C work from February 4th to April 1st 2008

Rev. 5

ID	Task Name	Status
19	Unbolt and crane out G-0 SMS upstream end cap.	Delayed
20	Remove lead blocks from end cap and bring to lead storage Bld.	Delayed
21	Unbolt and lift out down stream end cap	Delayed
22	Bolt both end caps together, seal for storage	Delayed
23	Change HMS actuators. General HMS maintenance	Delayed
24	Remove GEP beam line spool piece, leak check old window	Complete
25	RADCON support required	Complete
26	Change Berilium window and leak check	Complete
27	RADCON support required	Complete
28	Fabricate parts to modify beam dump connecting section and install	Delayed
29	RADCON support required	Delayed
30	Reinstall beam line spool piece and leak test beam pipe	Complete
31	RADCON support required	Complete
32	Pump out Moller cryo lines	Active
33	Crane BIG CAL into position	
34		
35		
36		

Project: 2008 Feb and March Hall C w
 Date: Tue 3/18/08

Rev. 5

Task		Project Summary	
Split		External Tasks	
Progress		External MileTask	
Milestone		Split	
Summary			

For information and changes contact the the Hall-C coordinator: Walter Kellner, ext. 5512, pager584-5512 , cell 592-1527

Hall C work from February 4th to April 1st 2008

Rev. 5

ID	Task Name	Status
37	<u>Cryo Target work on Pivot</u>	
38	Unbolt and remove scattering chamber windows	Complete
39	RADCON support required	Complete
40	Reconfigure the target cells and blocks for GeP in April.	Complete
41	RADCON support required	Complete
42	Align target cells	Complete
43	install new window o-rings	Complete
44	Bolt on windows	Complete
45	Leak test scattering chamber and target cells	Active
46	Vent scattering chamber	
47	Pump out target chamber and cool down for beam	
48		
49		
50	<u>Test installation for SANE Cherenkov counter and tracker</u>	
51	Remove pivot railing and platform extensions	Active
52	Install Cherenkov detector support frame, align and bolt to floor	Active
53	Install railing and staircase then secure staircase to platform	Active
54	Place Cherenkov on stand, about 10 cm back from SANE position	

Project: 2008 Feb and March Hall C w
 Date: Tue 3/18/08
Rev. 5

Task		Project Summary	
Split		External Tasks	
Progress		External MileTask	
Milestone		Split	
Summary			

For information and changes contact the the Hall-C coordinator: Walter Kellner, ext. 5512, pager584-5512 , cell 592-1527










Hall C work from February 4th to April 1st 2008

Rev. 5

ID	Task Name	Status
55	Connect HV and signal cables to Cherenkov	
56	Hook up gas flow system to Cherenkov	
57	Install SANE tracker between Cherenkov and target	
58	Install a few SANE Lucite counters, connect HV and signal cables	
59	Install new support stand for shielding, bolt to floor	Delayed
60	Weld bracket to Pivot and bolt down girder	Delayed
61	RADCON support required	Delayed
62	Fill 3 ALU boxes with painted lead bricks, crane onto girder and bolt down	Active
63	Crane in and place align 3 ALU shield boxes onto Pivot	
64	Place mounting angle brackets and weld to Pivot	
65	RADCON support required	
66	Fill boxes with lead painted bricks, crane onto Pivot and bolt down	
67	Remove aerial lifts and equipment, cleanup Hall and lock up	
68	BEAM, SANE test run	
69	Disconnect and remove Cherenkov detector and tracker	
70	RADCON support required	
71	Unbolt and crane 3 lead shielding boxes of Pivot	
72	RADCON support required	

Project: 2008 Feb and March Hall C w
Date: Tue 3/18/08

Rev. 5

Task		Project Summary	
Split		External Tasks	
Progress		External MileTask	
Milestone		Split	
Summary			

For information and changes contact the the Hall-C coordinator: Walter Kellner, ext. 5512, pager584-5512 , cell 592-1527










Hall C work from February 4th to April 1st 2008

Rev. 5

ID	Task Name	Status
73	Unbolt and crane 3 lead shielding boxes of Girder and store	
74	RADCON support required	
75	Remove railing and staircase from Cherenkove stand	

Project: 2008 Feb and March Hall C w
Date: Tue 3/18/08

Rev. 5

Task		Project Summary	
Split		External Tasks	
Progress		External MileTask	
Milestone		Split	
Summary			

For information and changes contact the the Hall-C coordinator: Walter Kellner, ext. 5512, pager584-5512 , cell 592-1527

Hall C work from February 4th to April 1st 2008 Rev. 5

Duration	Start	Finish	Risk Code #	Task Hazard Analysis	In Atlis	In HC List	Hot Work Permit
<u>36 days</u>	<u>Tue 2/12/08</u>	<u>Tue 4/1/08</u>					
1 day?	Wed 2/13/08	Wed 2/13/08	2	C-08-013-T			
1 day?	Tue 2/12/08	Tue 2/12/08	0	ITHA Req'd			
2 days?	Wed 2/13/08	Thu 2/14/08	0	ITHA Req'd			
2 days?	Wed 2/13/08	Thu 2/14/08	0	ITHA Req'd			
3 days?	Thu 2/14/08	Mon 2/18/08	1	ITHA Req'd			
3 days?	Mon 2/18/08	Wed 2/20/08	0	ITHA Req'd			
3 days?	Thu 2/21/08	Mon 2/25/08	1	ITHA Req'd			
15 days?	Thu 2/21/08	Wed 3/12/08	1	C-08-017-T			
2 days?	Mon 3/3/08	Tue 3/4/08	0	ITHA Req'd			
2 days?	Tue 2/26/08	Wed 2/27/08	2	C-08-001-T			
2 days?	Tue 2/26/08	Wed 2/27/08	0	ITHA Req'd			
6 days?	Tue 3/4/08	Tue 3/11/08	0	ITHA Req'd			Yes
4 days?	Tue 3/4/08	Fri 3/7/08	0	ITHA Req'd			
1 day?	Tue 3/4/08	Tue 3/4/08	1	C-08-003-T			
4 days?	Tue 3/4/08	Fri 3/7/08	0	ITHA Req'd			
1 day?	Wed 3/5/08	Wed 3/5/08	1	C-09-008-T			

Project: 2008 Feb and March Hall C w
Date: Tue 3/18/08

Task

Split

Progress

Milestone

Summary

Project Summary

External Tasks

External MileTask

Split

For information and changes contact the the Hall-C coordinator: Walter Kellner, ext. 5512, pager584-5512 , cell 592-1527

Hall C work from February 4th to April 1st 2008 Rev. 5

Duration	Start	Finish	Risk Code #	Task Hazard Analysis	In Atlis	In HC List	Hot Work Permit
1 day?	Thu 3/6/08	Thu 3/6/08	2	ITHA Req'd			
2 days?	Fri 3/7/08	Mon 3/10/08	1	Yes			
1 day?	Tue 3/11/08	Tue 3/11/08	2	ITHA Req'd			
1 day?	Wed 3/12/08	Wed 3/12/08	0	ITHA Req'd			
4 days?	Tue 3/18/08	Fri 3/21/08	0	ITHA Req'd		Yes	
2 days?	Wed 3/12/08	Thu 3/13/08	2	Yes	7225		
2 days?	Wed 3/12/08	Thu 3/13/08	0	ITHA Req'd			
3 days?	Fri 3/14/08	Tue 3/18/08	1	Yes			
3 days?	Fri 3/14/08	Tue 3/18/08	0	ITHA Req'd			
11 days?	Wed 3/5/08	Wed 3/19/08	1	ITHA Req'd		Yes	
3 days?	Fri 3/14/08	Tue 3/18/08	0	ITHA Req'd			
1 day?	Wed 3/19/08	Wed 3/19/08	1	Yes			
1 day?	Wed 3/19/08	Wed 3/19/08	0	ITHA Req'd			
1 day?	Tue 3/25/08	Tue 3/25/08	1	ITHA Req'd		Yes	
1 day?	Wed 3/26/08	Wed 3/26/08	1	ITHA Req'd			

Project: 2008 Feb and March Hall C w
Date: Tue 3/18/08

Rev. 5

Task		Project Summary	
Split		External Tasks	
Progress		External MileTask	
Milestone		Split	
Summary			

For information and changes contact the the Hall-C coordinator: Walter Kellner, ext. 5512, pager584-5512 , cell 592-1527

Hall C work from February 4th to April 1st 2008 Rev. 5

Duration	Start	Finish	Risk Code #	Task Hazard Analysis	In Atllis	In HC List	Hot Work Permit
<u>27 days?</u>	<u>Mon 2/25/08</u>	<u>Tue 4/1/08</u>			<u>7229</u>	<u>7</u>	
1 day?	Mon 3/3/08	Mon 3/3/08	1	Yes			
1 day?	Mon 3/3/08	Mon 3/3/08	0	ITHA Req'd			
1 day?	Wed 3/5/08	Wed 3/5/08	1	Yes			
1 day?	Wed 3/5/08	Wed 3/5/08	0	ITHA Req'd			
1 day?	Mon 3/10/08	Mon 3/10/08	1	Yes	Yes		
1 day?	Wed 3/12/08	Wed 3/12/08	0	ITHA Req'd			
1 day?	Wed 3/12/08	Wed 3/12/08	1	Yes			
1 day?	Mon 3/17/08	Mon 3/17/08	2	Yes		Yes	
1 day?	Tue 3/18/08	Tue 3/18/08	1	ITHA Req'd			
3 days?	Fri 3/28/08	Tue 4/1/08	2				
<u>12 days?</u>	<u>Mon 3/17/08</u>	<u>Tue 4/1/08</u>					
1 day?	Mon 3/17/08	Mon 3/17/08	1	Yes			
1 day?	Mon 3/17/08	Mon 3/17/08	0	ITHA Req'd			
1 day?	Mon 3/17/08	Mon 3/17/08	1	Yes			
1 day?	Tue 3/18/08	Tue 3/18/08	0	ITHA Req'd			

Project: 2008 Feb and March Hall C w
Date: Tue 3/18/08

Task Project Summary

Split External Tasks

Progress External MileTask

Milestone Split

Summary

For information and changes contact the the Hall-C coordinator: Walter Kellner, ext. 5512, pager584-5512 , cell 592-1527

Hall C work from February 4th to April 1st 2008 Rev. 5

Duration	Start	Finish	Risk Code #	Task Hazard Analysis	In Atllis	In HC List	Hot Work Permit
1 day?	Wed 3/19/08	Wed 3/19/08	0	ITHA Req'd			
1 day?	Thu 3/20/08	Thu 3/20/08	0	ITHA Req'd			
1 day?	Wed 3/19/08	Wed 3/19/08	1	Yes			
1 day?	Wed 3/19/08	Wed 3/19/08	1	Yes			
1 day?	Thu 3/20/08	Thu 3/20/08	0	Yes			
1 day?	Thu 3/20/08	Thu 3/20/08	0	ITHA Req'd			Yes
1 day?	Thu 3/20/08	Thu 3/20/08	0	ITHA Req'd	Yes		
2 days?	Fri 3/21/08	Mon 3/24/08	1	ITHA Req'd	Yes		
2 days?	Tue 3/25/08	Wed 3/26/08	1	Yes			
1 day?	Wed 3/26/08	Wed 3/26/08	1	Yes			Yes
1 day?	Wed 3/26/08	Wed 3/26/08	0	ITHA Req'd	Yes		
2 days?	Thu 3/27/08	Fri 3/28/08	1	ITHA Req'd			
1 day?	Mon 3/31/08	Mon 3/31/08	0	ITHA Req'd			
4 days?	Tue 4/1/08	Fri 4/4/08	1	ITHA Req'd			
1 day?	Fri 4/4/08	Fri 4/4/08	0	Yes			
1 day?	Fri 4/4/08	Fri 4/4/08	0	ITHA Req'd	Yes		
1 day?	Fri 4/4/08	Fri 4/4/08	1	Yes			
1 day?	Fri 4/4/08	Fri 4/4/08	0	ITHA Req'd			

Project: 2008 Feb and March Hall C w
Date: Tue 3/18/08

Rev. 5

Task		Project Summary	
Split		External Tasks	
Progress		External MileTask	
Milestone		Split	
Summary			

For information and changes contact the the Hall-C coordinator: Walter Kellner, ext. 5512, pager584-5512 , cell 592-1527

Hall C work from February 4th to April 1st 2008 Rev. 5

Duration	Start	Finish	Risk Code #	Task Hazard Analysis	In Atlas	In HC List	Hot Work Permit
1 day?	Fri 4/4/08	Fri 4/4/08	1	Yes			
1 day?	Fri 4/4/08	Fri 4/4/08	0	ITHA Req'd			
1 day?	Fri 4/4/08	Fri 4/4/08	1	Yes			

Project: 2008 Feb and March Hall C w
 Date: Tue 3/18/08

Rev. 5

- Task Project Summary
- Split External Tasks
- Progress External MileTask
- Milestone Split
- Summary

For information and changes contact the the Hall-C coordinator: Walter Kellner, ext. 5512, pager584-5512 , cell 592-1527

Hall C work from February 4th to April 1st 2008 Rev. 5

TOSP, RWP, Lift Plan	Risk Code #	Resource Names	Feb 10, '08							Feb 17, '08						
			S	M	T	W	T	F	S	S	M	T	W	T		
			C-08-007-L	0	Hall C Tech's											
	0	RADCON														
	0	Hall C Tech's														
	0	RADCON														
C-08-008-L	0	Hall C Tech's														
	0	Hall C Tech's														
	0	Hall C Tech's														
	0	Hall C Tech's														
	0	Hall C Tech's														
	1	Hall C Tech's														
	0	RADCON														
	0	Hall C Tech's														
	0	RADCON														
C-08-006-L	0	Hall C Tech's														

Project: 2008 Feb and March Hall C w
 Date: Tue 3/18/08
Rev. 5

Task		Project Summary	
Split		External Tasks	
Progress		External MileTask	
Milestone		Split	
Summary			

For information and changes contact the the Hall-C coordinator: Walter Kellner, ext. 5512, pager584-5512 , cell 592-1527

Hall C work from February 4th to April 1st 2008 Rev. 5

TOSP, RWP, Lift Plan	Risk Code #	Resource Names	Feb 10, '08							Feb 17, '08				
			S	M	T	W	T	F	S	S	M	T	W	T
			Lift plan	0	Hall C Tech's									
		Hall C Tech's												
Lift plan	0	Hall C Tech's												
	0	Hall C Tech's												
	0	Hall C Tech's												
RWP	0	Hall C Tech's / RADCON												
RWP	0	RADCON												
RWP	0	Hall C Tech's / ESH&Q												
RWP	0	RADCON												
RWP		Hall C Tech's / RADCON												
RWP	0	RADCON												
RWP		Hall C Tech's / RADCON												
RWP	0	RADCON												
	0	Hall C Tech's												
C-08-005-L	0	Hall C Tech's / Experim.												

Project: 2008 Feb and March Hall C w
Date: Tue 3/18/08

Rev. 5

Task		Project Summary	
Split		External Tasks	
Progress		External MileTask	
Milestone		Split	
Summary			

For information and changes contact the the Hall-C coordinator: Walter Kellner, ext. 5512, pager584-5512 , cell 592-1527

Hall C work from February 4th to April 1st 2008 Rev. 5

TOSP, RWP, Lift Plan	Risk Code #	Resource Names	Feb 10, '08						Feb 17, '08						
			S	M	T	W	T	F	S	S	M	T	W	T	
			<u>SOP</u>												
	0	Cryo Target Tech's													
	0	RADCON													
	0	Cryo Target Tech's													
	0	RADCON													
	0	Alignment Group													
	0	Hall C Tech's													
	0	Hall C Tech's													
	1	Cryo Target Tech's													
	0	Cryo Target Tech's													
Targ ops manu	0	Target Group / Experim.													
	0	Hall C Tech's													
	0	Hall C Tech's													
	0	Hall C Tech's													
	0	Hall C Tech's													

Project: 2008 Feb and March Hall C w
Date: Tue 3/18/08

Rev. 5

Task		Project Summary	
Split		External Tasks	
Progress		External MileTask	
Milestone		Split	
Summary			

For information and changes contact the the Hall-C coordinator: Walter Kellner, ext. 5512, pager584-5512 , cell 592-1527

Hall C work from February 4th to April 1st 2008 Rev. 5

TOSP, RWP, Lift Plan	Risk Code #	Resource Names	Feb 10, '08							Feb 17, '08				
			S	M	T	W	T	F	S	S	M	T	W	T
				0	Experimenters									
	0	Hall C Tech's												
	0	Hall C Tech's												
	0	Hall C Tech's / Experim.												
	0	Hall C Tech's												
	0	Hall C Tech's												
	0	Hall C Tech's												
	0	Hall C Tech's												
	0	Hall C Tech's												
	0	Hall C Tech's												
TOSP	0	Hall C Tech's / ESH&Q												
	0	Hall C Tech's												
	0	Hall C Tech's												
	0	Hall C Tech's												
TOSP	0	Hall C Tech's / ESH&Q												
	0	Hall C Tech's												
<i>Beam permit</i>	<i>0</i>	<i>Experimenters</i>												
	0	Hall C Tech's												
	0	Hall C Tech's												
	0	Hall C Tech's												
	0	Hall C Tech's												
	0	Hall C Tech's												

Project: 2008 Feb and March Hall C w
Date: Tue 3/18/08

Rev. 5

Task		Project Summary	
Split		External Tasks	
Progress		External MileTask	
Milestone		Split	
Summary			

For information and changes contact the the Hall-C coordinator: Walter Kellner, ext. 5512, pager584-5512 , cell 592-1527

Hall C work from February 4th to April 1st 2008 Rev. 5

TOSP, RWP, Lift Plan	Risk Code #	Resource Names	Feb 10, '08							Feb 17, '08				
			S	M	T	W	T	F	S	S	M	T	W	T
			0	Hall C Tech's										
0	RADCON													
0	Hall C Tech's													

--	--	--	--


Project: 2008 Feb and March Hall C w
Date: Tue 3/18/08

Rev. 5

Task		Project Summary	
Split		External Tasks	
Progress		External MileTask	◆
Milestone	◆	Split	↓
Summary			

For information and changes contact the the Hall-C coordinator: Walter Kellner, ext. 5512, pager584-5512 , cell 592-1527

Hall C work from February 4th to April 1st 2008 Rev. 5

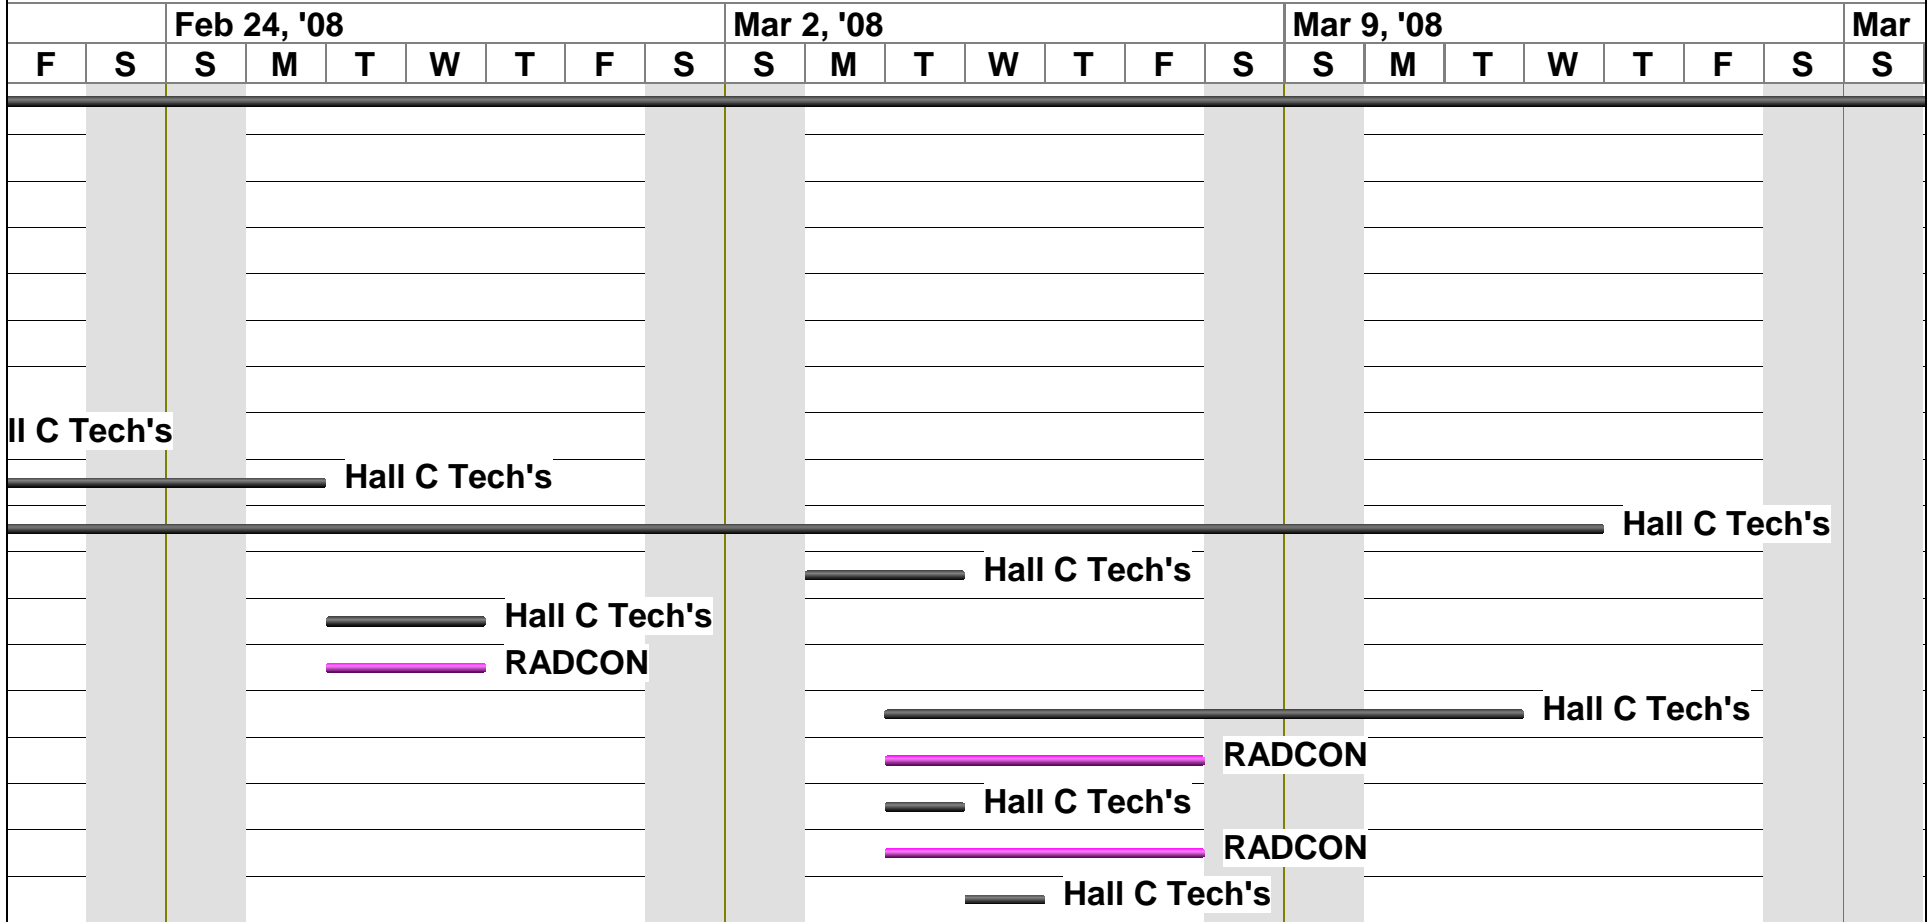


Project: 2008 Feb and March Hall C w
 Date: Tue 3/18/08
Rev. 5

Task		Project Summary	
Split		External Tasks	
Progress		External MileTask	
Milestone		Split	
Summary			

For information and changes contact the the Hall-C coordinator: Walter Kellner, ext. 5512, pager584-5512 , cell 592-1527

Hall C work from February 4th to April 1st 2008 Rev. 5

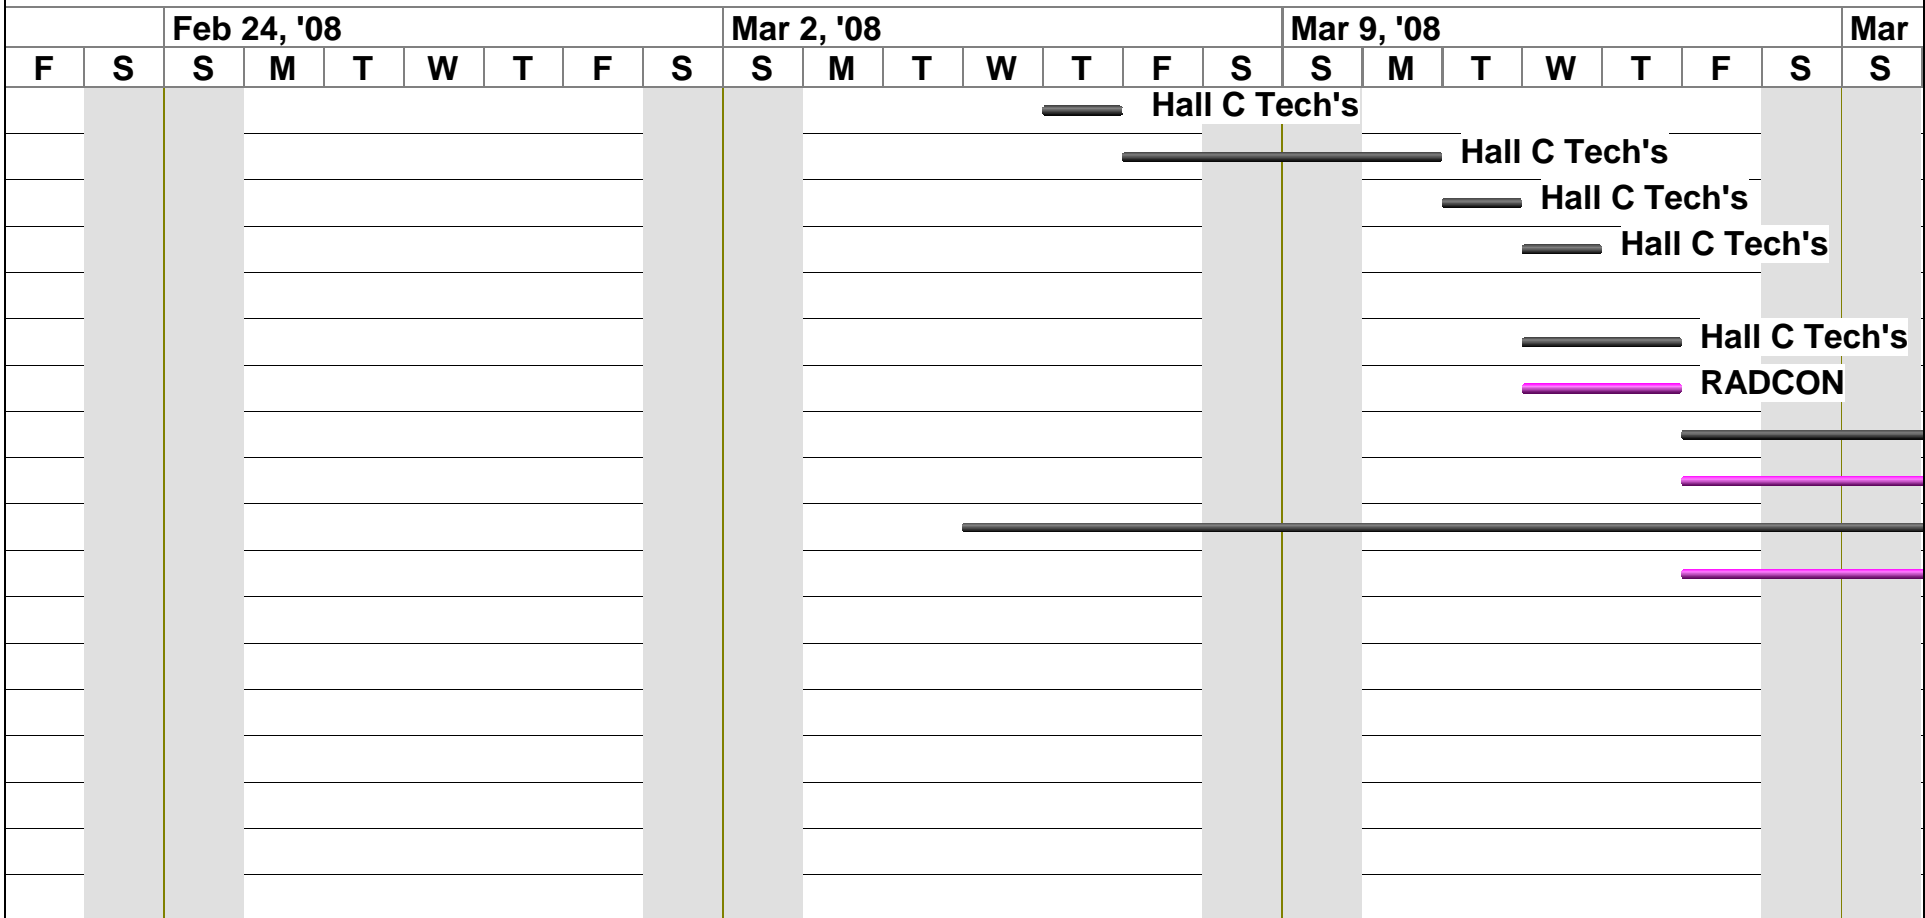


Project: 2008 Feb and March Hall C w
 Date: Tue 3/18/08
Rev. 5

Task		Project Summary	
Split		External Tasks	
Progress		External MileTask	
Milestone		Split	
Summary			

For information and changes contact the the Hall-C coordinator: Walter Kellner, ext. 5512, pager584-5512 , cell 592-1527

Hall C work from February 4th to April 1st 2008 Rev. 5

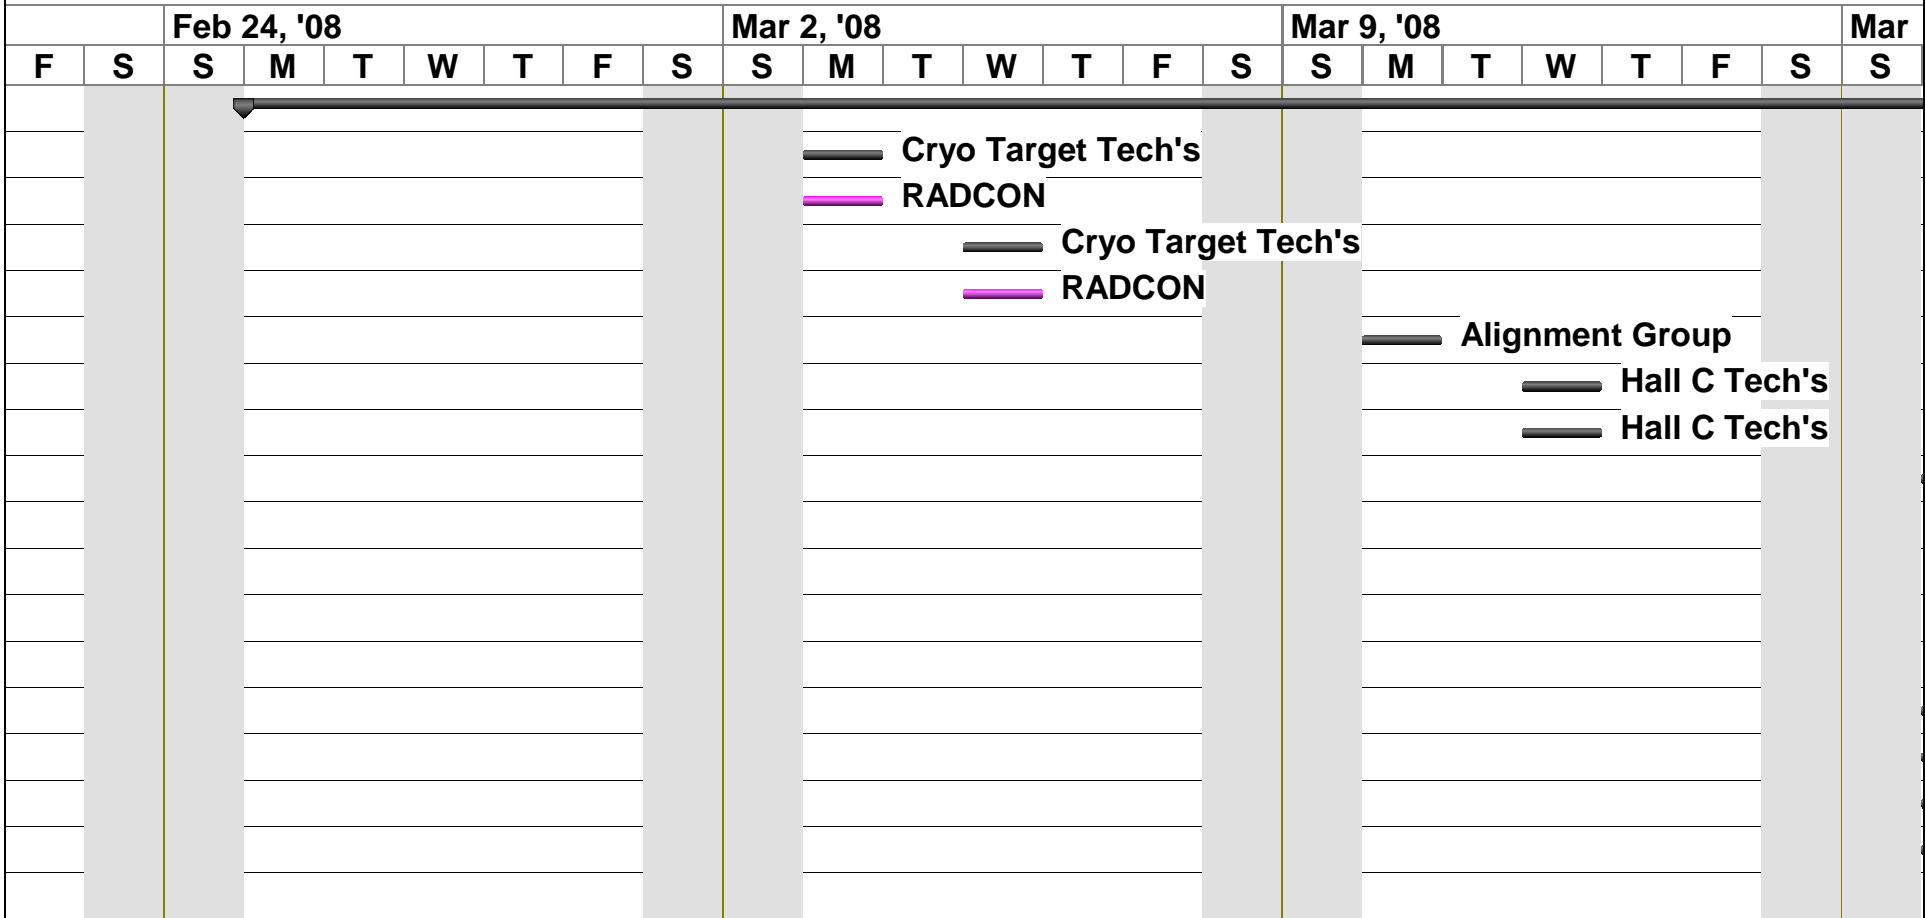

Project: 2008 Feb and March Hall C w
 Date: Tue 3/18/08
Rev. 5

Task		Project Summary	
Split		External Tasks	
Progress		External MileTask	
Milestone		Split	
Summary			

For information and changes contact the the Hall-C coordinator: Walter Kellner, ext. 5512, pager584-5512 , cell 592-1527

Hall C work from February 4th to April 1st 2008 Rev. 5

		Feb 24, '08							Mar 2, '08							Mar 9, '08							Mar
F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S

Project: 2008 Feb and March Hall C w
 Date: Tue 3/18/08
Rev. 5

Task		Project Summary	
Split		External Tasks	
Progress		External MileTask	◆
Milestone	◆	Split	↓
Summary			

For information and changes contact the the Hall-C coordinator: Walter Kellner, ext. 5512, pager584-5512, cell 592-1527

Hall C work from February 4th to April 1st 2008 Rev. 5

		Feb 24, '08							Mar 2, '08							Mar 9, '08							Mar
F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S




Project: 2008 Feb and March Hall C w
Date: Tue 3/18/08

Rev. 5

Task		Project Summary	
Split		External Tasks	
Progress		External MileTask	
Milestone		Split	
Summary			

For information and changes contact the the Hall-C coordinator: Walter Kellner, ext. 5512, pager584-5512 , cell 592-1527

Hall C work from February 4th to April 1st 2008 Rev. 5




Project: 2008 Feb and March Hall C w Date: Tue 3/18/08 Rev. 5	Task Project Summary
	Split External Tasks
	Progress External MileTask
	Milestone Split
	Summary

For information and changes contact the the Hall-C coordinator: Walter Kellner, ext. 5512, pager584-5512 , cell 592-1527

Hall C work from February 4th to April 1st 2008

Rev. 5

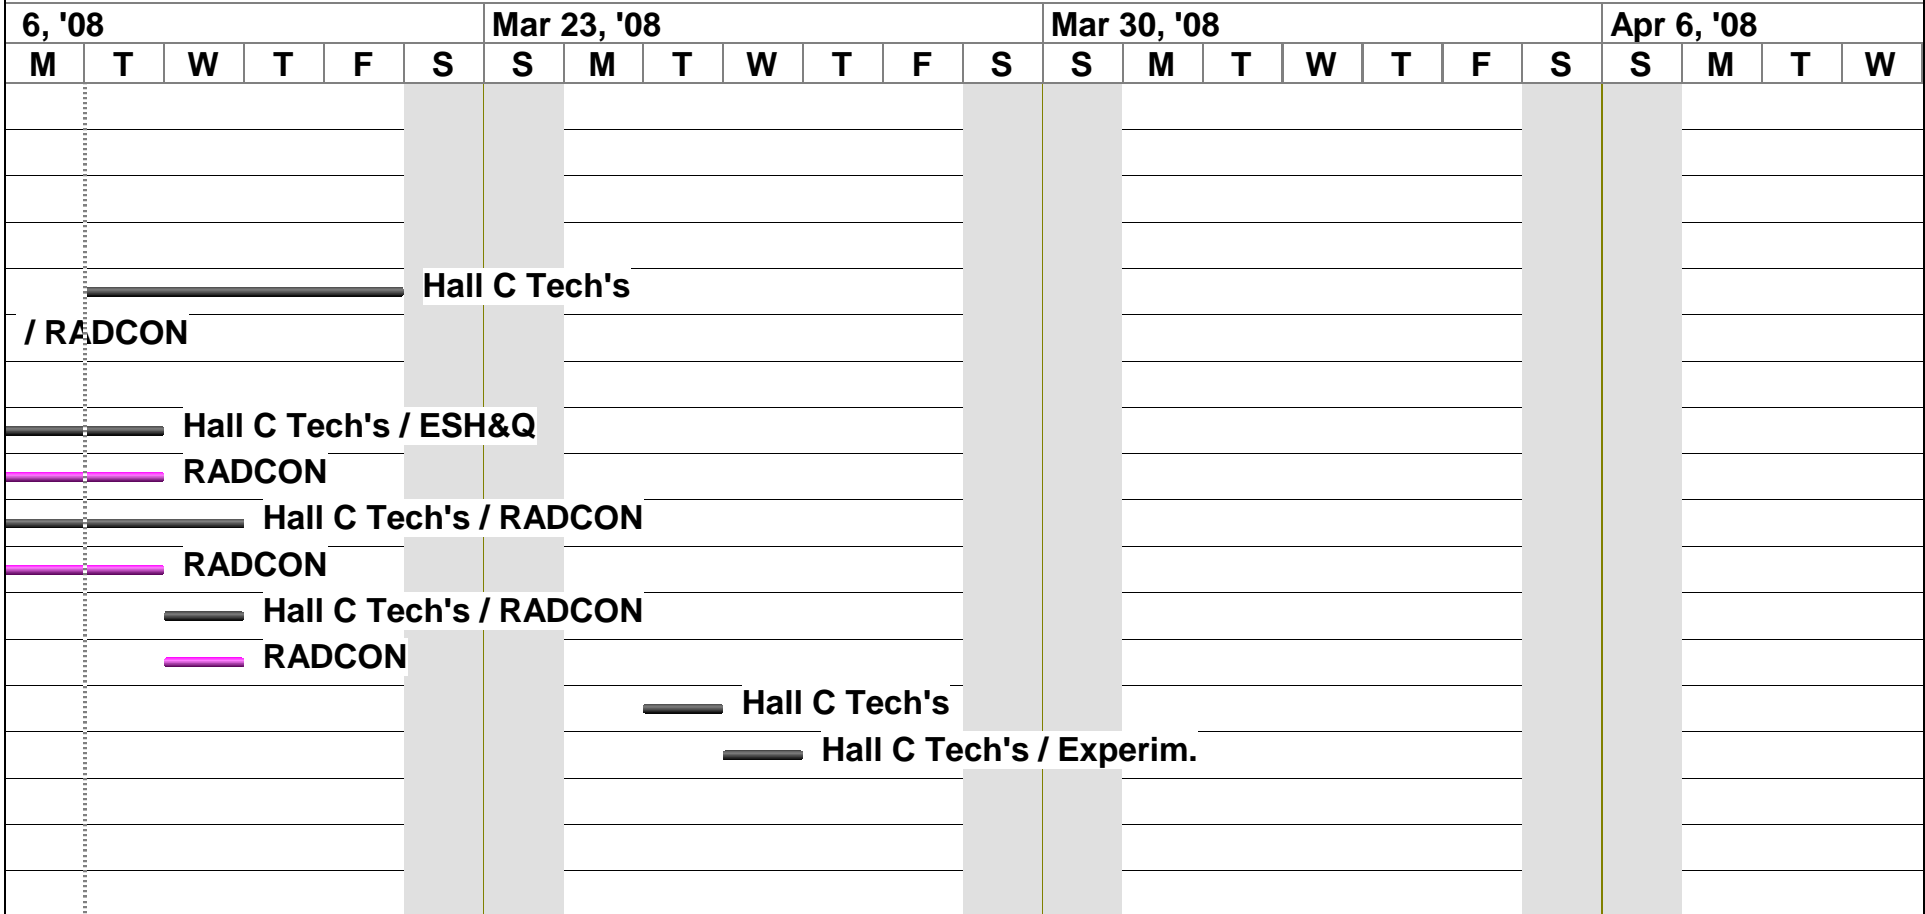


Project: 2008 Feb and March Hall C w
 Date: Tue 3/18/08
Rev. 5

Task		Project Summary	
Split		External Tasks	
Progress		External MileTask	
Milestone		Split	
Summary			

For information and changes contact the the Hall-C coordinator: Walter Kellner, ext. 5512, pager584-5512, cell 592-1527

Hall C work from February 4th to April 1st 2008

Rev. 5

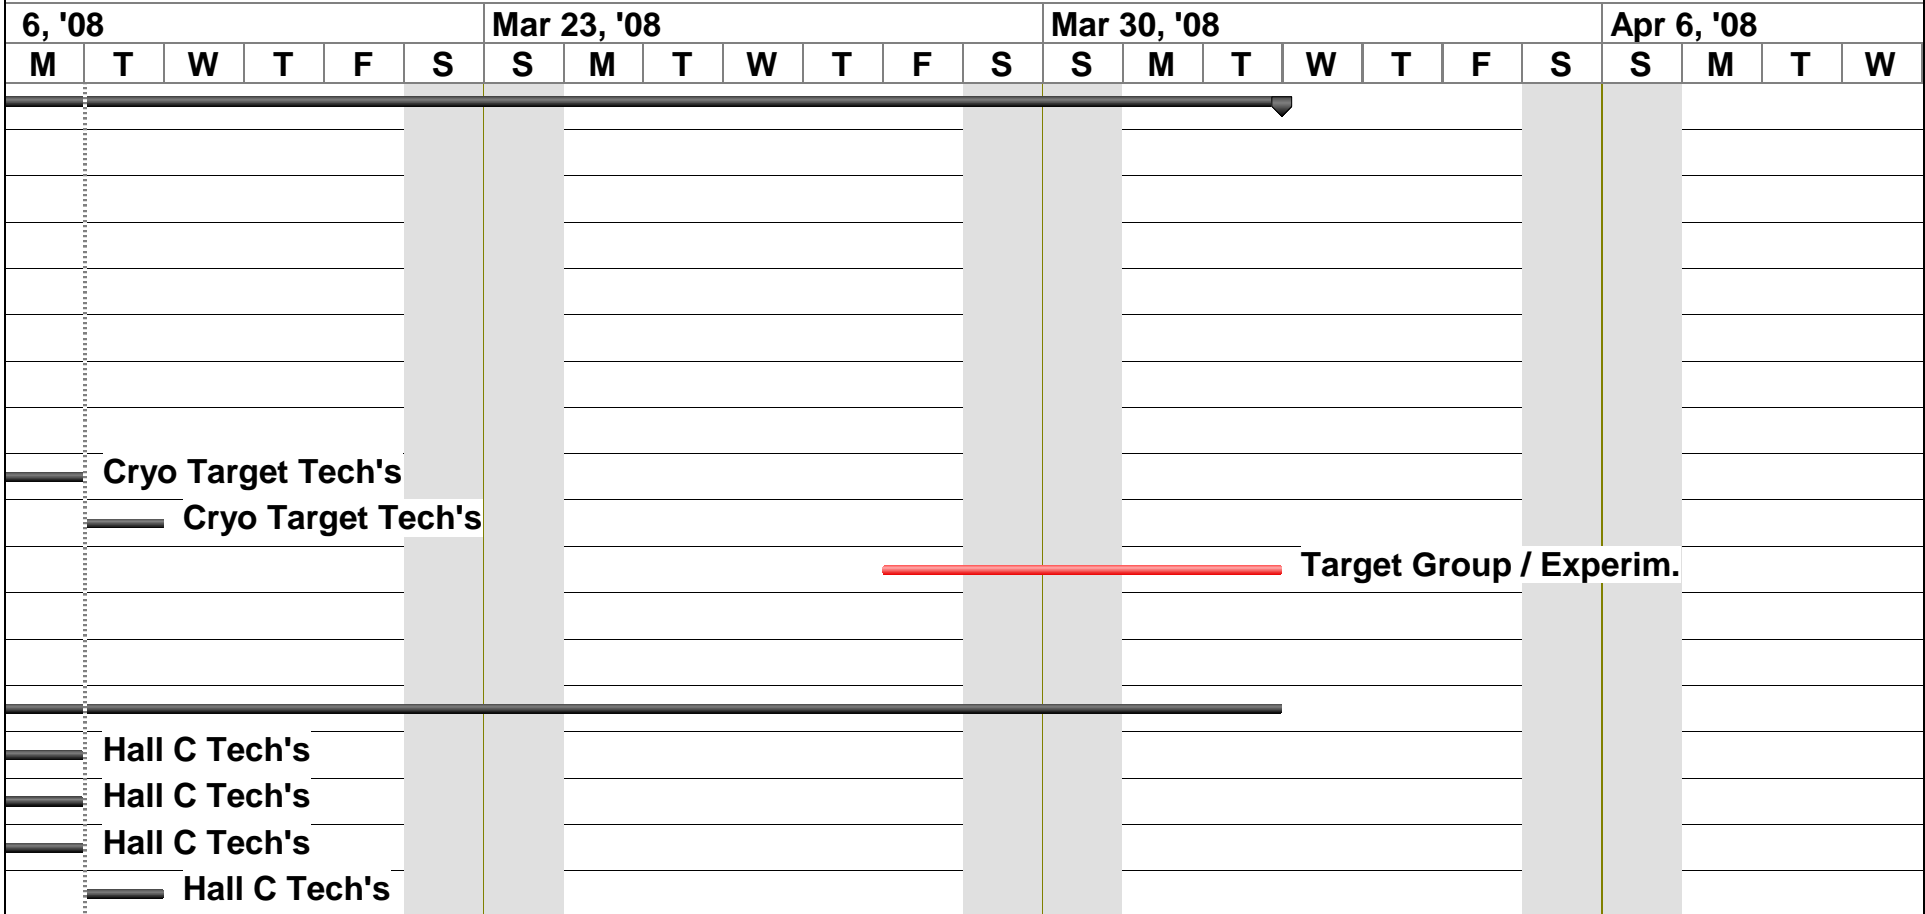


Project: 2008 Feb and March Hall C w
 Date: Tue 3/18/08
Rev. 5

Task		Project Summary	
Split		External Tasks	
Progress		External MileTask	
Milestone		Split	
Summary			

For information and changes contact the the Hall-C coordinator: Walter Kellner, ext. 5512, pager584-5512, cell 592-1527

Hall C work from February 4th to April 1st 2008

Rev. 5

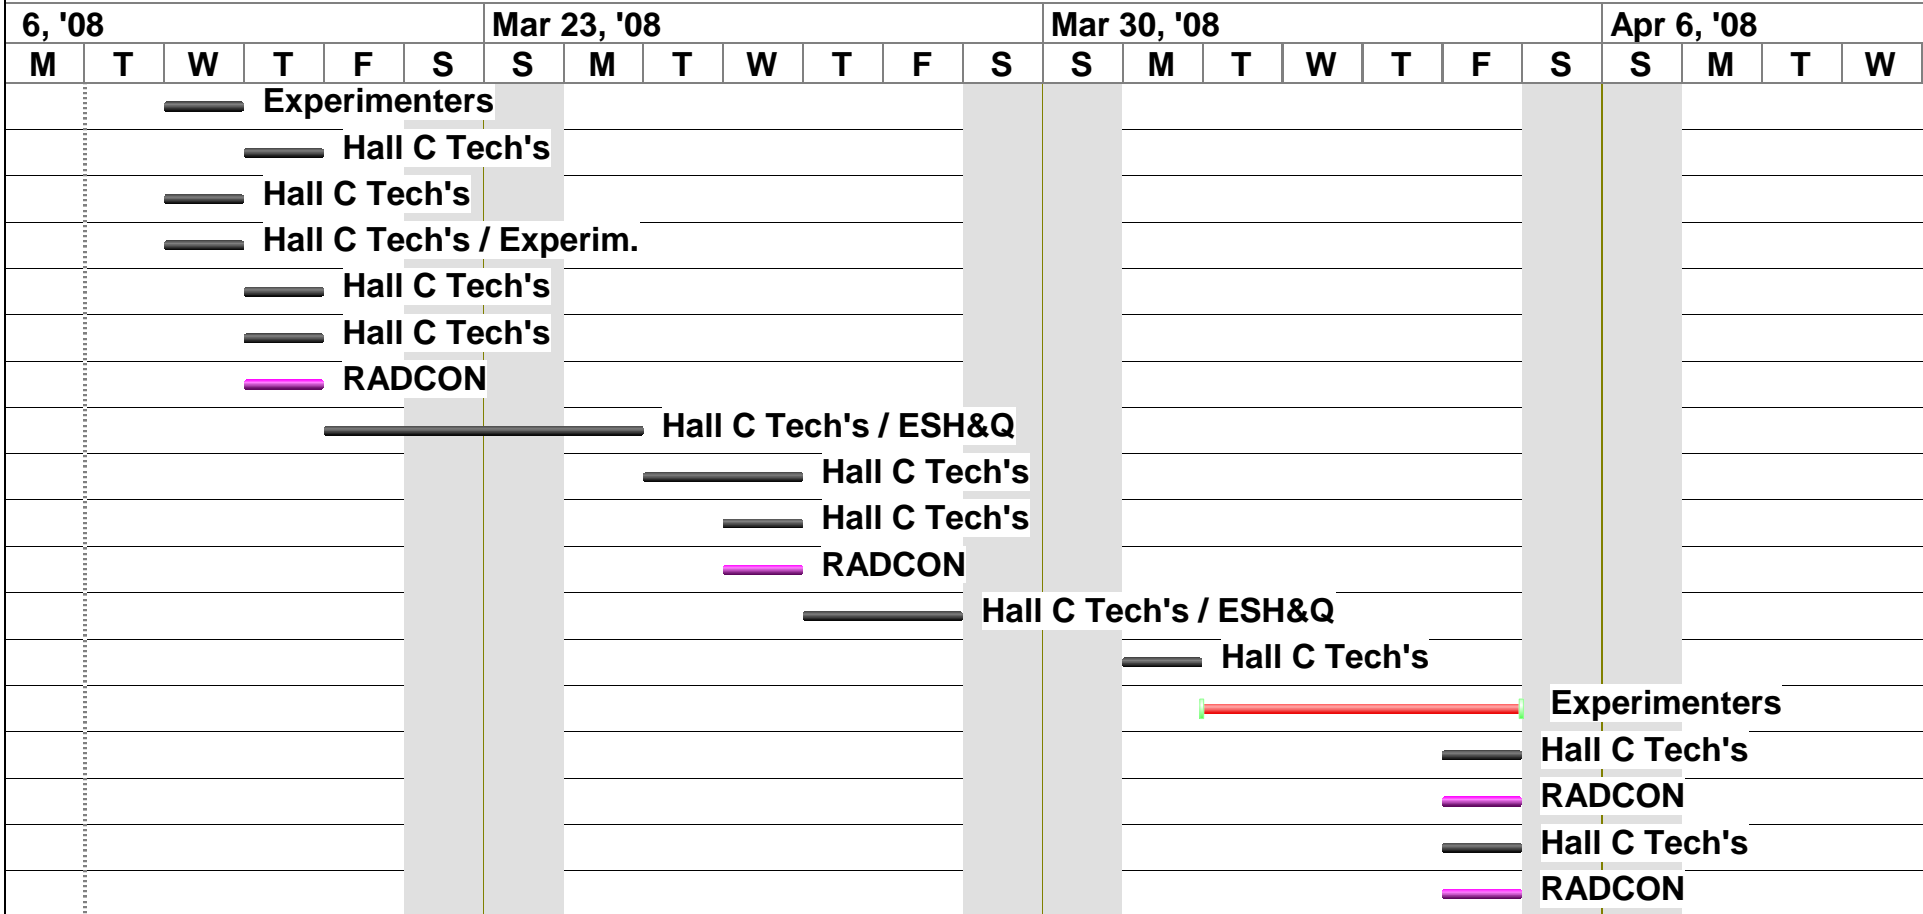

Project: 2008 Feb and March Hall C w
 Date: Tue 3/18/08
Rev. 5

Task		Project Summary	
Split		External Tasks	
Progress		External MileTask	
Milestone		Split	
Summary			

For information and changes contact the the Hall-C coordinator: Walter Kellner, ext. 5512, pager584-5512, cell 592-1527

Hall C work from February 4th to April 1st 2008 Rev. 5

6, '08						Mar 23, '08						Mar 30, '08						Apr 6, '08					
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W
																			▬	Hall C Tech's			
																			▬	RADCON			
																			▬	Hall C Tech's			

Project: 2008 Feb and March Hall C w
 Date: Tue 3/18/08
Rev. 5

Task		Project Summary	
Split		External Tasks	
Progress		External MileTask	
Milestone		Split	
Summary			

For information and changes contact the the Hall-C coordinator: Walter Kellner, ext. 5512, pager584-5512 , cell 592-1527
